




Project Completion Summary

- Project Title:** Garretson Blend Station Zone 3 Emergency Generator - Project No. 2019-05
- Location:** 506 East Ontario Avenue, Corona 92881. The Garretson Blend Station is located in the southeast corner of the intersection of Ontario Avenue and Magnolia Avenue as shown in Exhibit A.
- Description:** The Garretson Blend Station stores and blends water from the City's well collection system in a buried 2.0 million-gallon potable water storage tank. Two booster pump stations pump blended water from the tank to the City's Zone 3 and Zone 4 potable water distribution systems.
- The project provided a 1-megawatt diesel-engine driven emergency standby generator to produce power to operate the Zone 3 pump station if utility power is unavailable.
- Schedule:** Construction started on March 26, 2020 and was completed on January 6, 2021.
- Construction Cost:** \$598,722.98
- Funding:** Water Utility Fund 570

Garretson Blend Station Zone 3 Emergency Generator Project No. 2019-05

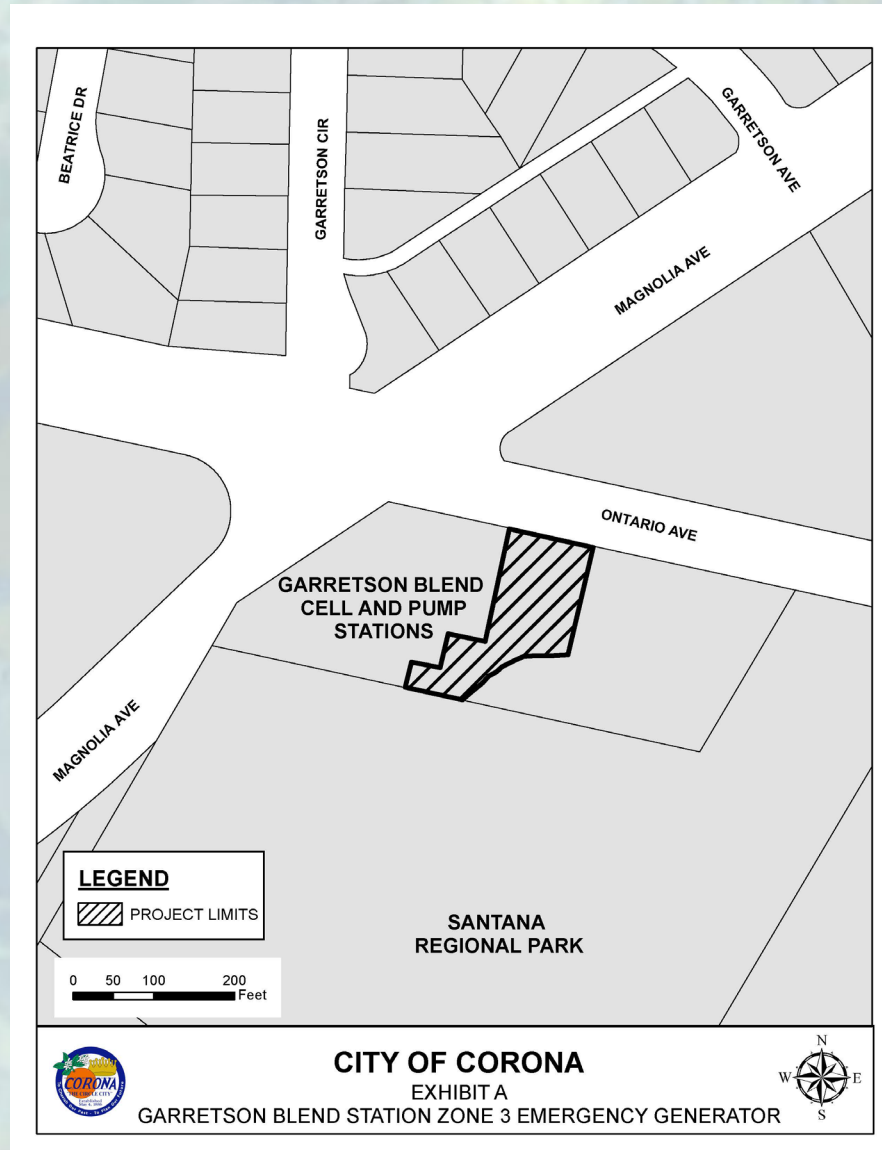

Garretson Blend Station Zone 3 Emergency Generator Project No. 2019-05



STRUCTURE EXCAVATION



**POWER CONDUITS
INSTALLATION**

Garretson Blend Station
Zone 3 Emergency Generator
Project No. 2019-05



**RETAINING WALLS CONSTRUCTED
PAD REINFORCING STEEL INSTALLED**



**FUEL TANK AND ENCLOSURE
INSTALLED ON PAD**

Garretson Blend Station
Zone 3 Emergency Generator
Project No. 2019-05



FUEL TANK



1 MW GENERATOR

Garretson Blend Station
Zone 3 Emergency Generator
Project No. 2019-05



***FUEL TANK AND GENERATOR ENCLOSURE INSIDE
SECURITY FENCING***
